

Start the Project

Assess Stakeholders

Data Gathering

- Questionnaires and surveys
- Brainstorming

Data Analysis


- Stakeholder analysis to understand their stakes, such as interests, rights, ownership, knowledge, and contribution
- Document analysis

dimensional (2D) grids
Power vs. Interest

- Power vs. Influence
- Impact vs. Influence
- Three-dimensional grid (Stakeholder cube)
- Salience model
- Directions of influence

Use two dimensions to map

© 2014 Pearson Education, Inc. or its affiliate(s). All rights reserved.

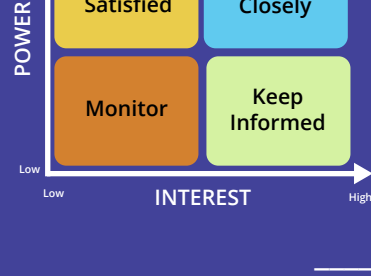

Use three dimensions (cube) to refine the analysis further



- Place each stakeholder on the grid (do not use names)
- Use the same quadrant labels but change the axis labels

Abstract

Stakeholder	Onboard	Resistant	Neutral	Supportive	Leading
1	-	-	-	D	C
2	-	-	-	C	D
3	-	-	C	D	-
4	-	-	C	D	-
5	-	C	D	-	-
6	-	-	-	C	D


C: Current engagement level; D: Desired engagement level

Approach	Description	Key Roles	Value Delivery
----------	-------------	-----------	----------------



Predictive or Plan-driven	Plan-based approach: - Activities completed in a distinct or linear fashion - New phase begins only when the previous phase is completed.	- Project sponsor authorizes project. - Team led by project manager	- Deliverables transitioned to customer at completion - Value realized in both short -and long-term
Adaptive or Agile	Change-based approach: - Agile, incremental, or iterative development - Time-boxed cadence (iteration or sprints) or continuous flow	- Product owner controls value proposition. - Project team delivers work. - Process roles include team lead, scrum master, agile coach, and facilitator.	- Iterative or incremental delivery to customer during life cycle - Regular customer feedback cycle enables continuous development of value toward a <i>final</i> product.
Hybrid	Any combination of the above		

Characteristics of Different Approaches

Approach	Characteristics	Certainty of Requirements	Change and Risk
Predictive or Plan-driven	- Plan-driven - Linear sequence of activities, in phases - Phase completion governed by phase gates	High, from beginning	- Controlled change possible - Risks carefully studied and managed
Adaptive or Agile	- Change-driven - Iterative or incremental - Time-boxed cadence (iterations or sprints) or continuous flow	Unclear or customer-driven, so needs further discovery	- Built on assumption of high degree of change - High tolerance of risk with guardrails for risk management
Hybrid	Tailored development approach, combining elements from both methodologies		

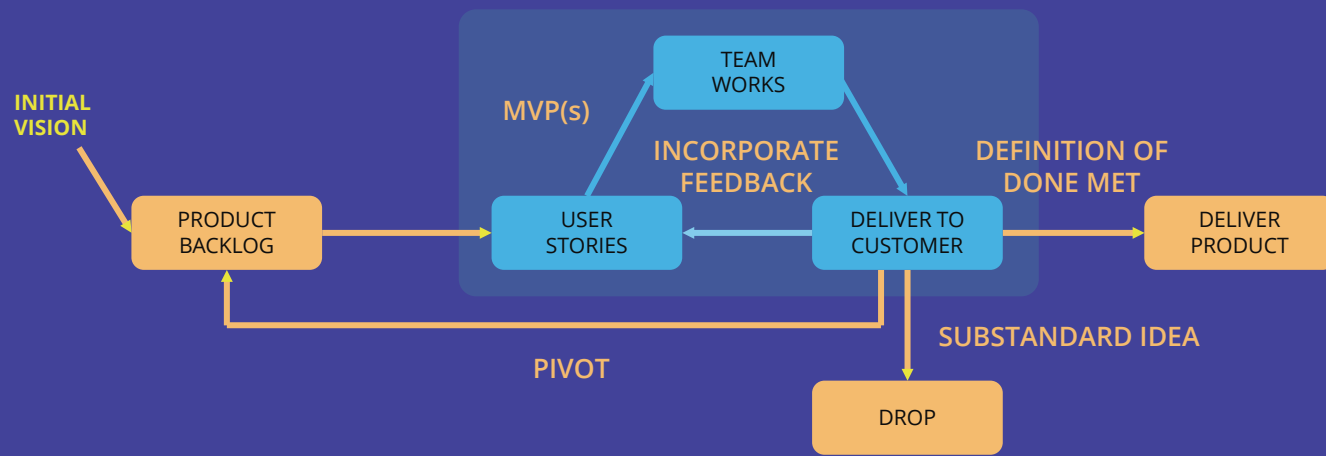

Tuckman's Stages of Team Formation

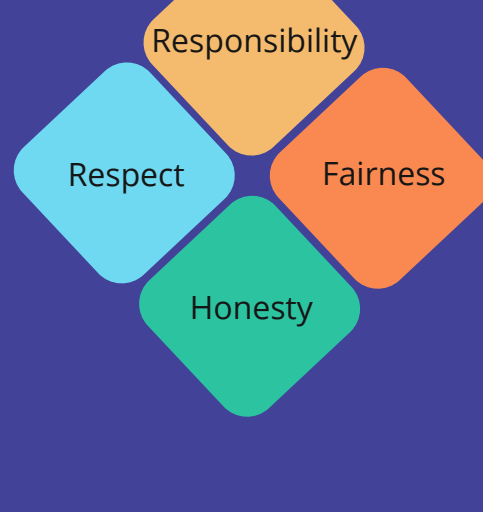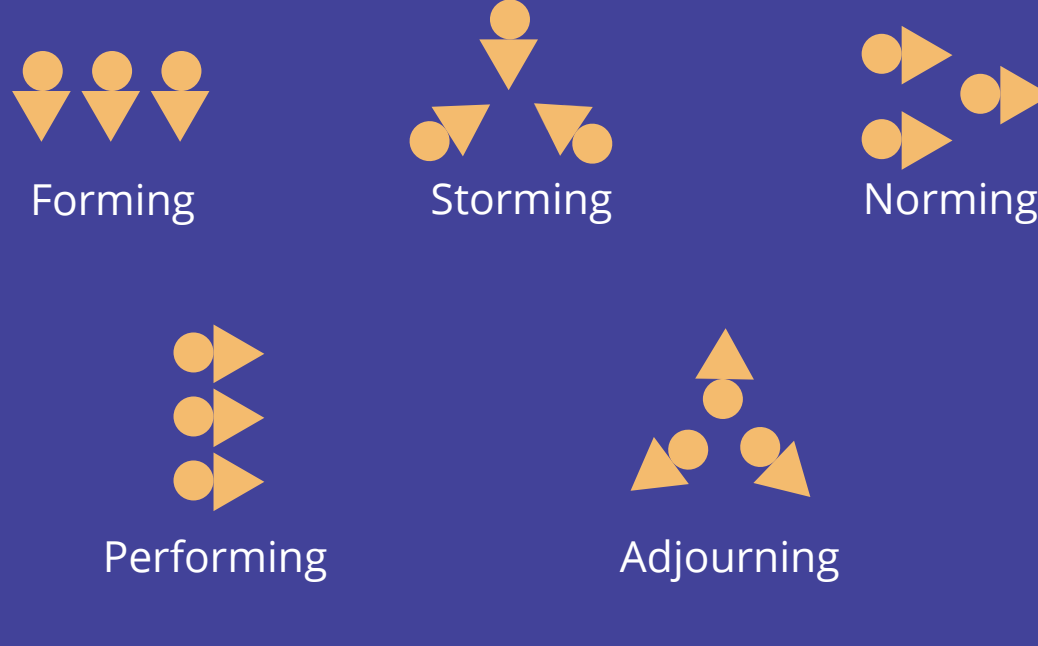

© 2010 Pearson Education, Inc. or its affiliate(s). All rights reserved.

